



**PROJECT PARTNER**

**YvY Capital**

**SPRINT 1 DELIVERABLE**

# **Delivery Roadmap**

Sprints 2-5 | Weeks 3-10

Data Governance Pipeline and Analytics

Prepared for YvY Capital | Inteli Special Projects | August 2026

Confidential - for project stakeholders only

# What we commit to deliver

A two-week sprint cadence with a concrete demonstration and partner decision at each gate.

## SPRINT 2

### Validated product direction

Clickable wireframes, prioritized use cases, KPI definitions, data-flow draft and an approved development backlog.

## SPRINT 3

### Working MVP alpha

Automated data pipeline v1 and a usable application covering NAV, portfolio, performance and internal fund comparison.

## SPRINT 4

### Integrated beta

Risk analytics, reconciliation, governance controls, peer comparison if data is available, plus user testing and documentation drafts.

## SPRINT 5

### Final product and handover

Stabilized application, production-ready pipeline, governance pack, manuals, source package and final demonstration.

## Product outcome

A governed data pipeline and a decision-support DataApp that replace fragmented email-based reporting with a consolidated, traceable view of fund NAV, portfolio composition, performance and risk.

## How YvY Capital participates

- Join the end-of-sprint review and provide consolidated feedback.
- Approve or reject each decision gate within the sprint review window.
- Confirm business rules, KPI definitions and data availability.
- Nominate users for beta validation before Sprint 4 closes.

# Product scope and delivery principles

The visual language can evolve; the agreed business capabilities and governance controls remain the delivery baseline.

## MVP capabilities

- Daily NAV and portfolio dashboard with fund and date selection.
- Per-fund performance view with returns and risk-return indicators.
- Comparison across the company's own funds.
- Automated reconciliation and visible data-quality exceptions.
- External peer benchmarking, subject to the ANBIMA data handoff.

## Supporting deliverables

- Data governance structure covering quality, security and traceability.
- Data flow diagram with source, intermediate and curated layers.
- Usage, operation and maintenance manuals.
- Test evidence, known limitations and handover package.

## Non-negotiable controls

- LGPD-sensitive data is anonymized or masked.
- Real fund names and partner names are excluded from processed repository data.
- Source-to-output lineage and quality checks are documented.
- Project materials remain in the authorized private environment.
- No visual copy of the current tool is required; UX will be validated with YvY.

## Scope-freeze decision criteria

### USER VALUE

Supports a recurring portfolio decision or removes manual reconciliation.

### DATA FEASIBILITY

Uses available, governed data or has an approved dependency plan.

### DELIVERY FIT

Can be built, tested and handed over within the remaining eight weeks.


## Sprint 2 scope freeze

Before development starts, YvY Capital will validate the target users, approved screen set, KPI logic, active fund universe, priority data sources and the treatment of peer benchmarking. Features not approved at this gate move to the post-MVP backlog.

Planning basis: Inteli Special Projects Guide, Project Charter, Feature Guide, Data Dictionary and current-tool demonstration.

# Global delivery plan

Each sprint lasts two weeks and closes with a delivery, demonstration and partner decision.

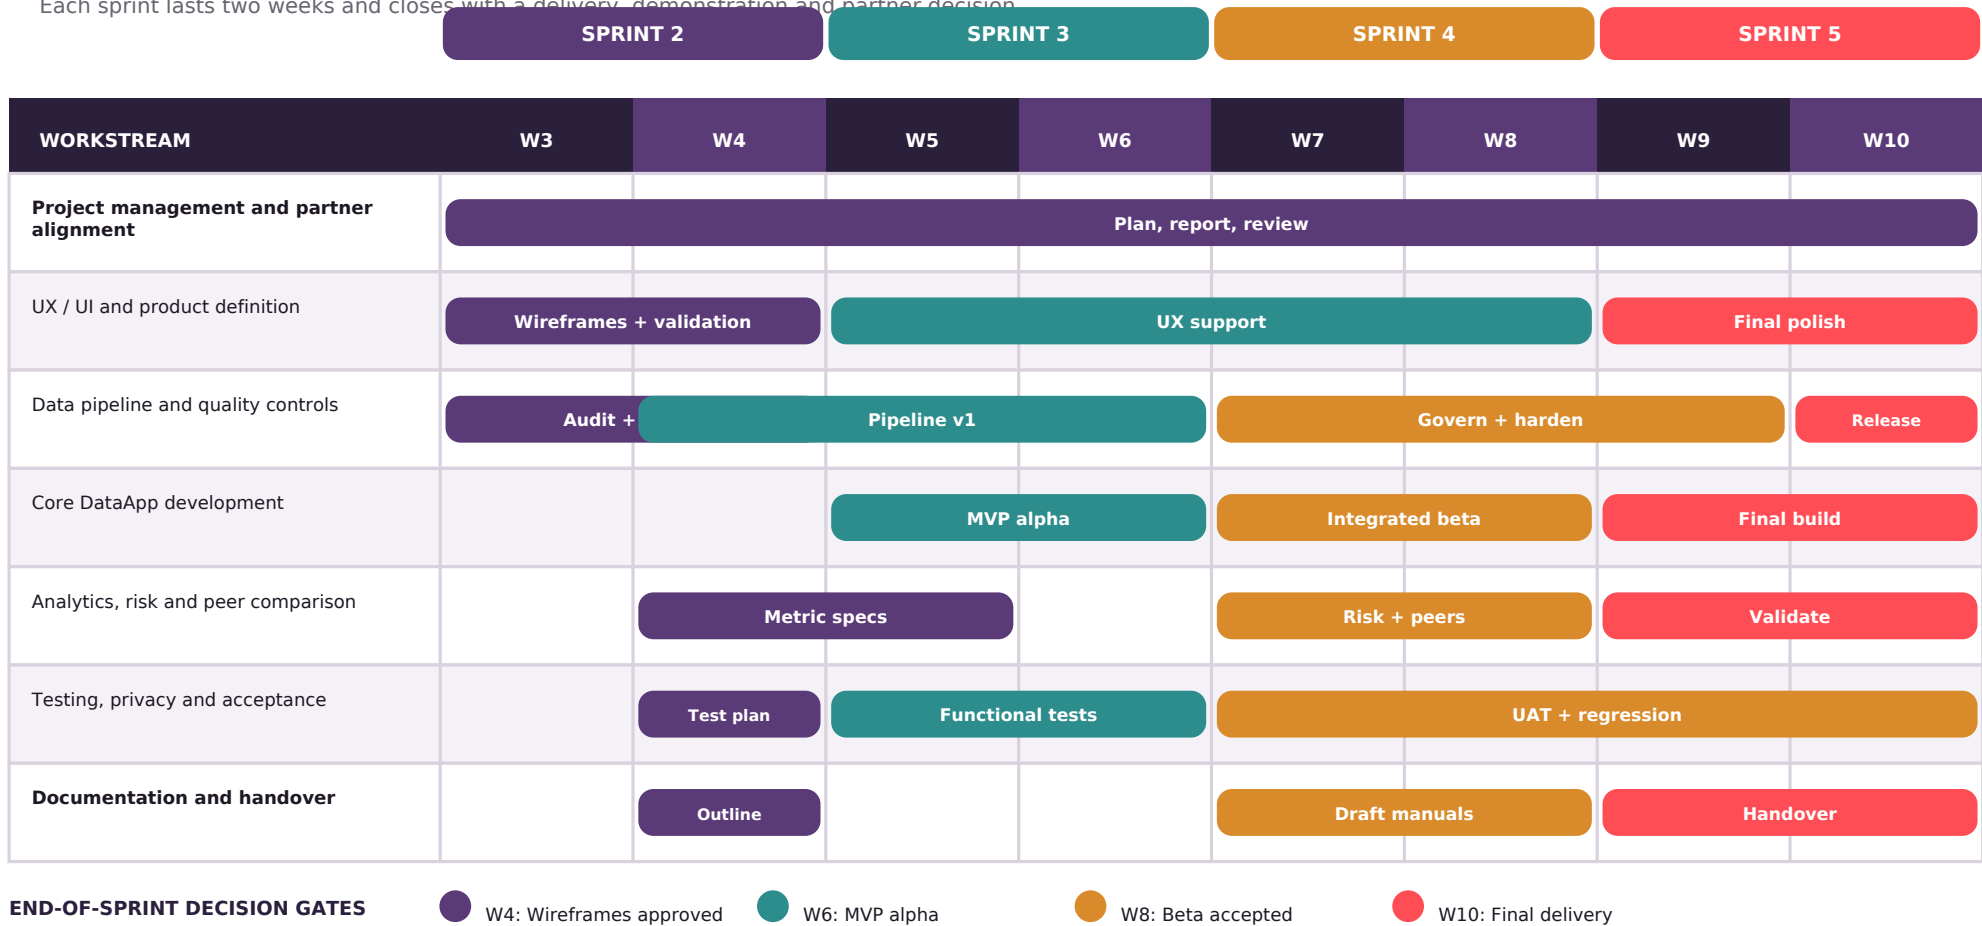

# Sprint 2 - Product definition and UX validation

Weeks 3-4 | Two-week delivery cycle

## OBJECTIVE

Convert the project charter and source data into an approved product direction before real application development starts.

### WEEK 3

- Interview needs and confirm priority users and decisions.
- Audit available datasets, gaps, joins and privacy constraints.
- Map user journeys and draft low-fidelity screens.
- Draft KPI definitions and the source-to-screen map.

### WEEK 4

- Viktor produces clickable wireframes and interaction states.
- Refine the data-flow diagram and technical architecture.
- Prioritize the MVP backlog and define acceptance criteria.
- Present the prototype to YvY and capture one decision set.

## Deliverables presented to YvY Capital

| Deliverable                                      | Primary owner    | Evidence at review                                                    |
|--------------------------------------------------|------------------|-----------------------------------------------------------------------|
| Clickable wireframe package and screen inventory | Viktor           | Fund selection, overview, performance, portfolio and comparison flows |
| KPI and calculation catalog                      | Isiah            | Definitions, formulas, source columns and assumptions                 |
| Data audit and data-flow draft                   | Adrien           | Availability, quality gaps, masking and layer proposal                |
| Architecture and prioritized backlog             | Raphael / Thomas | Technical approach, user stories and sprint-ready acceptance criteria |

## Partner decision gate

Approve the target users, screen set, navigation, KPI definitions, active fund universe, MVP boundary and peer-data treatment. Development begins only from the approved baseline.

## Team leads

Thomas: coordination and scope. Viktor: UX owner. Adrien, Isiah and Raphael: data, analytics and technical feasibility.

## Done when

One approved prototype baseline and a development-ready backlog exist.

# Sprint 3 - Pipeline foundation and MVP alpha

Weeks 5-6 | Two-week delivery cycle

## OBJECTIVE

**Build the first working product increment on top of a reproducible, governed data pipeline.**

### WEEK 5

- Implement ingestion, normalization and curated data layers.
- Add schema, completeness, uniqueness and reconciliation checks.
- Build the application shell, fund picker and navigation.
- Implement NAV and portfolio overview components.

### WEEK 6

- Add performance chart and internal fund comparison.
- Connect approved KPI calculations to curated datasets.
- Run functional tests and sample reconciliations.
- Demonstrate the working MVP alpha to Yvy Capital.

## Deliverables presented to Yvy Capital

| Deliverable                             | Primary owner   | Evidence at review                                            |
|-----------------------------------------|-----------------|---------------------------------------------------------------|
| ETL pipeline v1 and data-quality report | Adrien          | Repeatable run, curated outputs, checks and logged exceptions |
| Working MVP alpha                       | Raphael         | Fund selection, NAV, portfolio, performance and comparison    |
| Validated calculation notebook / module | Isiah           | Reproducible returns and agreed KPI samples                   |
| Sprint demo and issue backlog           | Thomas / Viktor | Usability feedback, defects and bounded changes               |

## Partner decision gate

Approve the core workflow, source interpretation, calculation logic and information hierarchy. Confirm which alpha issues are blocking versus backlog items.

## Team leads

Adrien: pipeline. Raphael: app build. Isiah: calculations. Viktor: UX review. Thomas: delivery gate.

## Done when

The alpha runs on approved anonymized data and demonstrates the core decision journey.

# Sprint 4 - Integrated analytics beta

Weeks 7-8 | Two-week delivery cycle

## OBJECTIVE

**Complete the analytical depth, governance controls and end-to-end user experience required for partner validation.**

### WEEK 7

- Add volatility, Sharpe/Sortino, drawdown and liquidity views.
- Parse validated stress-risk and DV01 results.
- Integrate peer data if available; otherwise validate the adapter and placeholder.
- Add reconciliation exceptions and lineage evidence.

### WEEK 8

- Run end-to-end, privacy and UAT tests.
- Refine accessibility, responsiveness and empty/error states.
- Complete governance and data-flow drafts.
- Demo the integrated beta and agree the final correction list.

## Deliverables presented to Yvy Capital

| Deliverable                           | Primary owner    | Evidence at review                                            |
|---------------------------------------|------------------|---------------------------------------------------------------|
| Integrated beta application           | Raphael / Viktor | Complete flows, responsive states and beta demonstration      |
| Risk and benchmarking module          | Isiah            | Documented formulas and peer behavior based on available data |
| Governance and lineage pack v1        | Adrien           | Controls, ownership, quality evidence and data-flow diagram   |
| UAT results and final correction list | Thomas           | Test evidence, severity, owner and target resolution          |

## Partner decision gate

Accept the beta or provide one prioritized, bounded list of required corrections. Confirm final deployment/handover expectations and the peer feature's final status.

## Team leads

Raphael and Viktor: integrated experience.  
Adrien: governance. Isiah: analytics. Thomas: UAT and scope control.

## Done when

All approved MVP journeys are testable end to end and only bounded final fixes remain.

# Sprint 5 - Final product and handover

Weeks 9-10 | Two-week delivery cycle

## OBJECTIVE

**Stabilize, document and deliver the complete approved solution with evidence that it is usable, traceable and maintainable.**

### WEEK 9

- Resolve accepted beta defects and complete regression testing.
- Harden pipeline monitoring, quality checks and error handling.
- Finalize UI details, performance and release configuration.
- Complete manuals and rehearse the end-to-end handover.

### WEEK 10

- Run the final controlled pipeline and application build.
- Deliver source, governance, data-flow and manual packages.
- Present the final product and known limitations.
- Transfer operating knowledge and agree the future backlog.

## Deliverables presented to Yvy Capital

| Deliverable                                  | Primary owner    | Evidence at review                                       |
|----------------------------------------------|------------------|----------------------------------------------------------|
| Final DataApp and release package            | Raphael / Viktor | Approved workflows, final UI and deployment instructions |
| Production-ready ETL and governance evidence | Adrien           | Repeatable pipeline, controls, lineage and release log   |
| Final analytics validation pack              | Isiah            | Formulas, sample reconciliations and limitations         |
| Manuals, final presentation and handover     | Thomas           | Usage, maintenance, acceptance and next-step backlog     |

## Partner decision gate

Confirm that the approved acceptance baseline is met, acknowledge documented limitations and accept the final application, pipeline and handover package.

## Team leads

All members own final QA and demonstration. Thomas coordinates acceptance; each functional lead hands over their component.

## Done when

The final package is complete, reproducible, demonstrated and accepted against the agreed baseline.

# Team allocation and accountability

Proposed ownership balances product, UX, data, analytics, engineering and delivery control.

## Thomas Duberseuil

### DELIVERY COORDINATION

Roadmap, scope, partner alignment, quality gate and final synthesis.

## Viktor Suzyumov

### UX / UI LEAD

Wireframes, interaction flows, design system and usability consistency.

## Adrien Cognet

### DATA ENGINEERING LEAD

Ingestion, transformation, data model, quality controls and lineage.

## Isiah Perelman

### ANALYTICS AND VALIDATION

KPI logic, risk metrics, peer methodology, test scenarios and UAT.

## Raphael Lefevere

### APPLICATION ENGINEERING LEAD

Architecture, application build, integration, performance and release.

## Responsibility matrix

| Activity                                 | TD  | VS | AC  | IP  | RL  |
|------------------------------------------|-----|----|-----|-----|-----|
| Partner alignment and sprint reporting   | A/R | C  | C   | C   | C   |
| Product scope and UX validation          | A   | R  | C   | C   | C   |
| Data pipeline and governance             | C   | I  | A/R | C   | C   |
| KPI and risk methodology                 | C   | C  | C   | A/R | C   |
| Application architecture and integration | C   | C  | C   | C   | A/R |
| Testing and acceptance evidence          | A   | C  | R   | R   | R   |
| Documentation and final handover         | A/R | C  | C   | C   | R   |

Legend: A = Accountable, R = Responsible, C = Consulted, I = Informed. Ownership is reviewed at every sprint planning session; each critical deliverable has at least one reviewer outside the lead function.

## Cross-review rules

### SCOPE + UX

Thomas and Viktor jointly review screen intent, prioritization and partner-facing clarity.

### DATA + APP

Adrien and Raphael verify that each screen is supported by reproducible curated data.

### METRICS + QA

Isiah independently checks formulas; all members execute acceptance scenarios.

# What YvY Capital will see each week

A concise weekly checkpoint keeps decisions early and prevents late rework.

| Week | Team output                                          | Shown to YvY Capital                                              | Feedback / decision                            |
|------|------------------------------------------------------|-------------------------------------------------------------------|------------------------------------------------|
| W3   | User journeys, data audit, screen inventory          | Low-fidelity flows and open business questions                    | Confirm users, priorities and missing rules    |
| W4   | Clickable wireframes, KPI catalog, backlog           | Sprint 2 prototype and proposed data flow                         | Approve UX, KPI set and MVP scope              |
| W5   | Pipeline foundation and application shell            | Early ingestion evidence and navigation shell                     | Confirm data interpretation and navigation     |
| W6   | MVP alpha with core dashboards                       | Working NAV, portfolio, performance and internal comparison views | Approve core workflow and calculation logic    |
| W7   | Risk analytics, reconciliation, beta integration     | Risk views, exception handling and beta progress                  | Prioritize corrections and peer scope          |
| W8   | Integrated beta, UAT evidence, manuals draft         | End-to-end beta demonstration                                     | Accept beta or issue a bounded correction list |
| W9   | Release candidate, regression and handover rehearsal | Near-final product and documentation review                       | Approve final fixes and handover plan          |
| W10  | Final application, pipeline, governance and manuals  | Final demonstration and complete delivery package                 | Final acceptance and transition                |

## Working cadence

Weekly written status: completed, next, risks, decisions.  
End-of-sprint review: live demo, evidence, feedback and written acceptance. Critical blockers are raised as soon as identified, not held for the review.

## Feedback standard

YvY Capital provides one consolidated response per review: Approved, Approved with bounded changes, or Not approved with the blocking reasons and priority corrections.

## Standard review agenda

### 1 DEMO

Working increment

### 2 EVIDENCE

Checks and test results

### 3 DECISIONS

Approvals and changes

### 4 ACTIONS

Owners and deadlines

# Dependencies, controls and acceptance

The plan is achievable if scope decisions and data access are resolved at the scheduled gates.

## Key delivery risks

| Risk / dependency                                     | Impact                                            | Planned control                                                                       |
|-------------------------------------------------------|---------------------------------------------------|---------------------------------------------------------------------------------------|
| Active fund universe or business rules remain unclear | Rework in data model and screens                  | Freeze scope and KPI catalog at the Sprint 2 gate                                     |
| Peer-fund data arrives late or changes shape          | Peer benchmarking cannot be completed on schedule | Build an adapter and mock view; integrate real data when the approved extract arrives |
| Sensitive data appears in source or output            | LGPD and confidentiality exposure                 | Mask identifiers, restrict access and run repository/output scans                     |
| Calculation definitions are not approved              | Conflicting performance or risk results           | Document formulas, assumptions and sample reconciliations before implementation       |
| Partner feedback is fragmented or delayed             | Sprint spillover and late redesign                | Use one consolidated response and fixed end-of-sprint decision gates                  |

### Final acceptance baseline

- Core approved journeys work end to end.
- Figures reconcile to agreed source samples.
- Automated quality checks and exceptions are visible.
- Privacy, masking and access constraints are respected.
- Data flow, governance and manuals are delivered.
- Known limitations and next-step backlog are explicit.

### Immediate next step

YvY Capital validates this roadmap, nominates the Sprint 2 reviewers and confirms the product workshop. The team then starts Week 3 with user journeys, data audit and Viktor's wireframe workstream.

Requested partner response: roadmap approval, named reviewers and confirmation of the Sprint 2 validation meeting.

Confidentiality: This document is intended only for Inteli and YvY Capital project stakeholders. Project data and presentations must not be shared outside the authorized project environment.

Prepared by: Thomas Duberseuil, Viktor Suzyumov, Adrien Cognet, Isiah Perelman and Raphael Lefevere.
