

INTELI × YVY CAPITAL

FUNDS MANAGER

SPRINT 2 — WEEK 1

PROGRESS REPORT

Dashboard Prototype, Current Capabilities and Path to the Final Product

Working Draft — Pending Partner Review

August 22, 2026

Project deliverable prepared by the Inteli student team in partnership with YvY Capital.

Prototype evidence only | Synthetic and aliased data | Not a production release

EXECUTIVE SUMMARY

Executive Summary

Verified progress, current boundaries, and the decisions needed to move from prototype to product.

CURRENT POSITION

Sprint 2 Week 1 has produced a coherent English-language interactive prototype that demonstrates the target information hierarchy and two priority journeys. It is not a production application: the displayed values are synthetic, role selection is simulated, and partner approval remains pending.

9 Live dashboard sections Every section executes and was inspected.	10 Demonstration scenarios Current, delayed, incomplete, empty, error, denied, and related states.
2 Priority user journeys Executive exploration and Analyst validation.	100% English UI coverage Visible and accessible copy checked in the DOM.

Sprint 2 Week 1 Objectives

- Translate priority user needs and the Sprint 1 roadmap into a demonstrable navigation and screen baseline.
- Expose fund, performance, comparison, quality, import, and lineage concepts without presenting synthetic evidence as certified business data.
- Make assumptions, freshness, quality, and unavailable prerequisites visible at the point of use.
- Create evidence for partner review before production development and before the Sprint 2 exit gate is claimed.

Pending partner validation - The prototype is a working draft; no YvY Capital approval is represented in this report.

Evidence basis: the verified dashboard, the project charter, the Sprint 1 delivery roadmap, the internal sprint plan, the Feature Guide, the Data Dictionary, and the Sprint 2 audit/remediation evidence.

WEEK 1 DELIVERY

Work Completed During the Week

The work is organized as a partner-reviewable product definition package, not as a claim of production readiness.

Interface	All navigation, cards, tables, scenarios, modals, notifications, filters, accessible labels, and dynamic workflow copy translated into consistent institutional English.
Executive journey	Overview -> Funds -> Fund Detail / Allocation -> Performance -> Internal Comparison -> Peer Comparison, with functional navigation and fund drill-down.
Analyst journey	Import -> structure control -> anomaly review -> quarantine -> validation -> local synthetic publication -> lineage, implemented as an interactive simulation.
Governance cues	Visible source, run, freshness, quality, hypothesis, quarantine, and lineage indicators; synthetic and sample states remain explicit.
Verification	Every page and scenario combination tested; allocation drill-down, modal, keyboard navigation, responsive layouts, and console behavior checked.

Dashboard Navigation and Information Architecture

Navigation group	Sections	Decision supported
Executive	Overview; Funds; Allocation; Performance; Comparison; Peers	Move from portfolio signal to fund detail and comparative context.
Operations	Data Quality; Import & Validation; Runs & Lineage	Inspect controls, simulate governed processing, and trace published evidence.
Global context	Fund, period, prototype scenario, user journey	Keep user context visible across sections.

IMPORTANT BOUNDARY

No production data connector, authentication, role-based authorization, external publication, or final financial certification is demonstrated. The role selector and publication path are prototype controls.

DASHBOARD SCREENS

Executive Overview

Point-by-point review of the live translated screen.

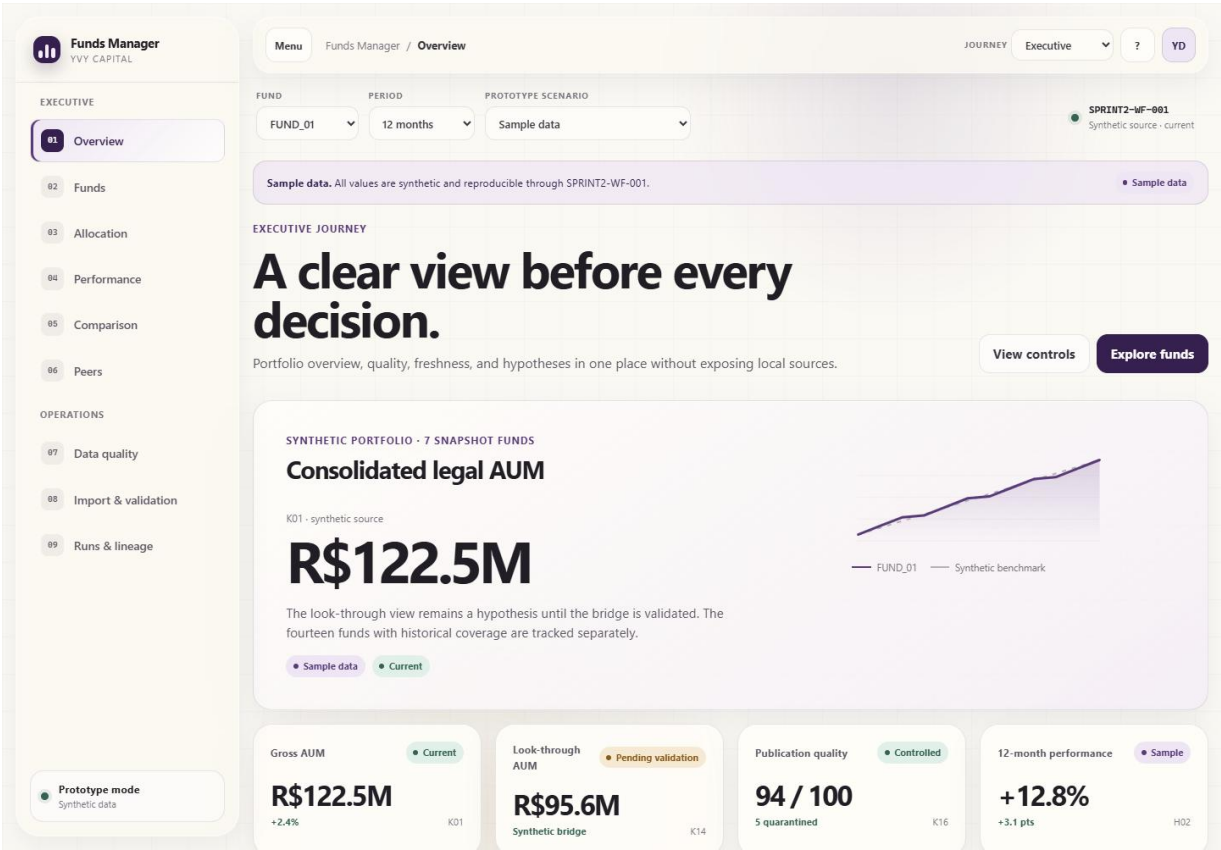


Figure 1. Executive Overview with navigation, global context, sample-data disclosure, portfolio signal, chart, and KPI cards.

Objective / user	Daily portfolio orientation for Executive users.
Displayed	Consolidated legal AUM, look-through hypothesis, publication quality, 12-month sample performance, priority funds, and alerts.
Visuals	One indexed line chart, four KPI cards, fund table, and alert list.
Filters / actions	Fund, period, scenario, journey; View controls and Explore funds.
Data states	Sample, current, late, incomplete, loading, empty, error, denied, no match, and hypothesis.
Data / limits	Synthetic values from the local prototype Serving payload; no production NAV or AUM certification.
Product contribution	Establishes the decision-first landing page and makes trust signals visible beside portfolio metrics.
Status	Implemented and visible - screen behavior is verified; business values remain sample data.

DASHBOARD SCREENS

Funds, Fund Detail and Allocation

One fund universe screen and one combined detail/allocation screen are currently present.

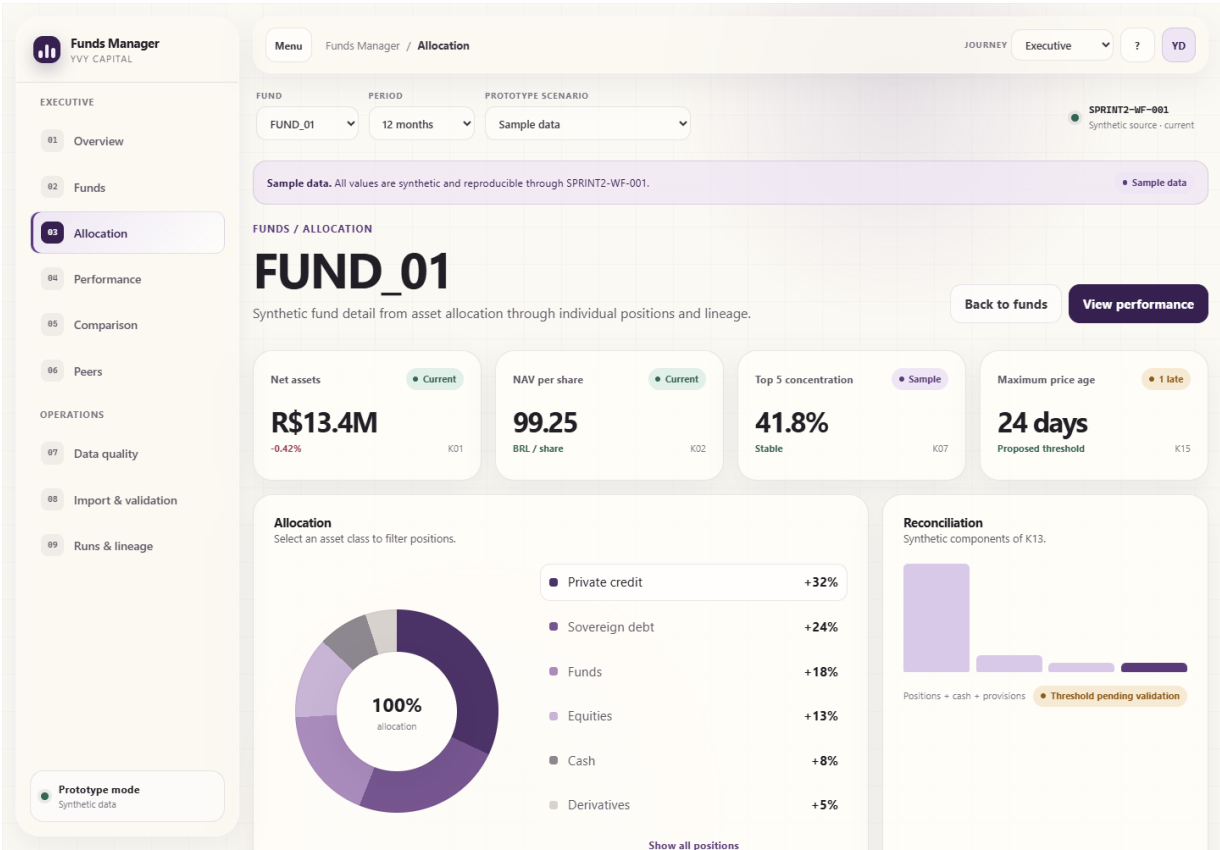


Figure 2. FUND_01 detail with KPI cards, interactive allocation, reconciliation summary, and a filtered holdings table below the viewport.

Funds screen	Lists 14 aliased funds, differentiates history-only from snapshot-plus-history coverage, and supports search and fund selection.
Detail objective	Explain one selected fund from net assets and NAV per share through asset allocation and individual positions.
KPIs	Net assets, NAV per share, Top 5 concentration, and maximum price age.
Visuals / tables	Interactive allocation donut, reconciliation mini-bars, and holdings table with issuer, value, weight, and price freshness.
Actions	Select fund; filter holdings by asset class; reset filter; continue to performance or return to funds.
Drill-down	Allocation segment -> filtered positions is functional and keyboard-accessible through buttons.
Limits	FUND_01 synthetic positions are reused as the demonstration detail baseline; no live position or NAV reconciliation.
Product contribution	Defines the portfolio transparency path and the evidence needed for future automated reconciliation.
Status	Interactive prototype - navigation and allocation drill-down work with synthetic fixtures.

DASHBOARD SCREENS

Performance, Risk and Internal Comparison

Historical analytics are shown as controlled sample outputs; not all final risk inputs are available.

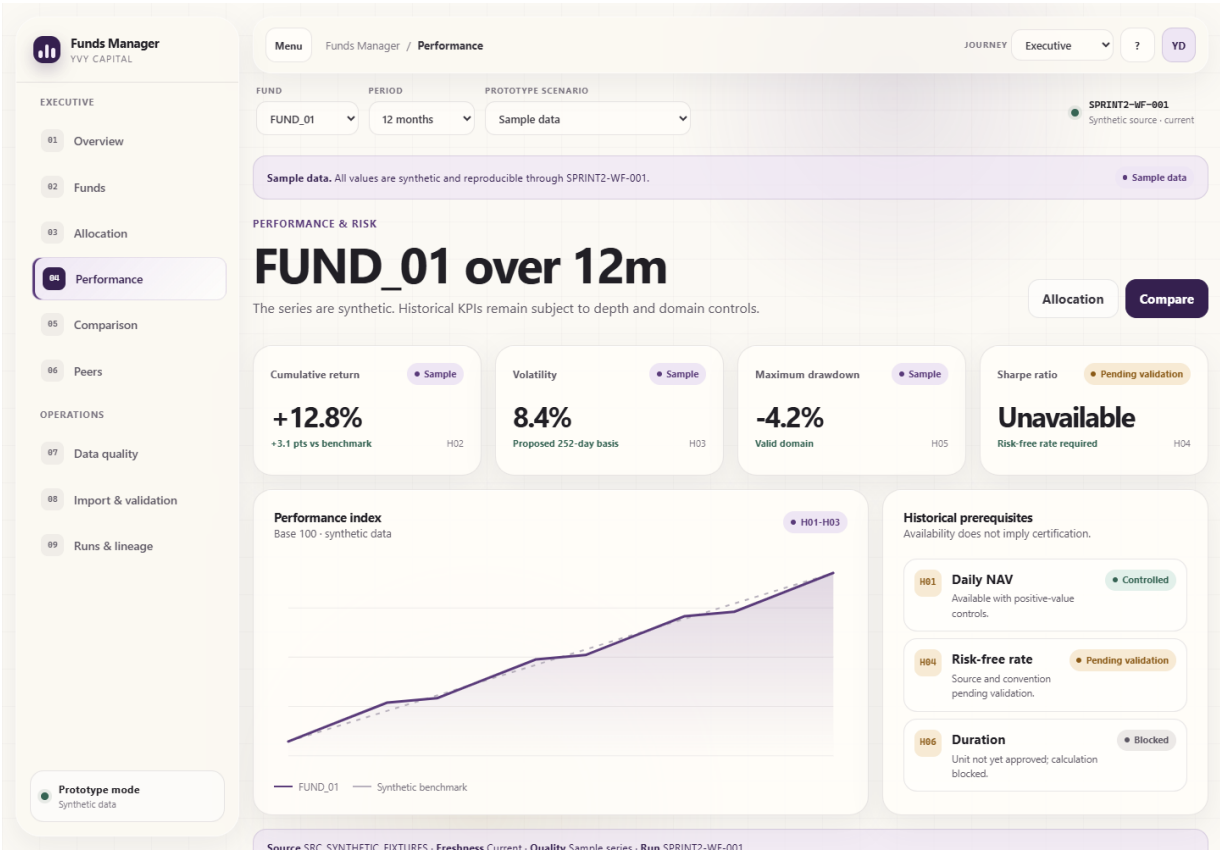


Figure 3. Performance and Risk view with a base-100 chart, sample metrics, and explicit prerequisite states.

Performance objective	Review one fund over the selected period against a synthetic benchmark.
KPIs / chart	Cumulative return, volatility, maximum drawdown, Sharpe availability, and one base-100 comparison chart.
Prerequisites	Daily NAV is marked controlled; risk-free rate is pending validation; duration is blocked until its unit is agreed.
Internal Comparison	Seven snapshot funds are compared at one date by AUM, relative size, daily return, volatility, and quality.
Filters / actions	Fund and period selection; links back to Allocation and forward to Comparison / Peers.
States	Incomplete and hypothesis states modify metric availability without silently substituting values.
Limits	Displayed analytics are synthetic; formula certification, approved reference datasets, and production history are not demonstrated.
Product contribution	Defines the final analytical hierarchy while protecting users from unsupported metrics.
Status	Partially implemented - views exist; final calculation modules and reference reconciliations remain future work.

DASHBOARD SCREENS

Peer Comparison

The interface is deliberately separated from any claim that an external peer universe is certified.

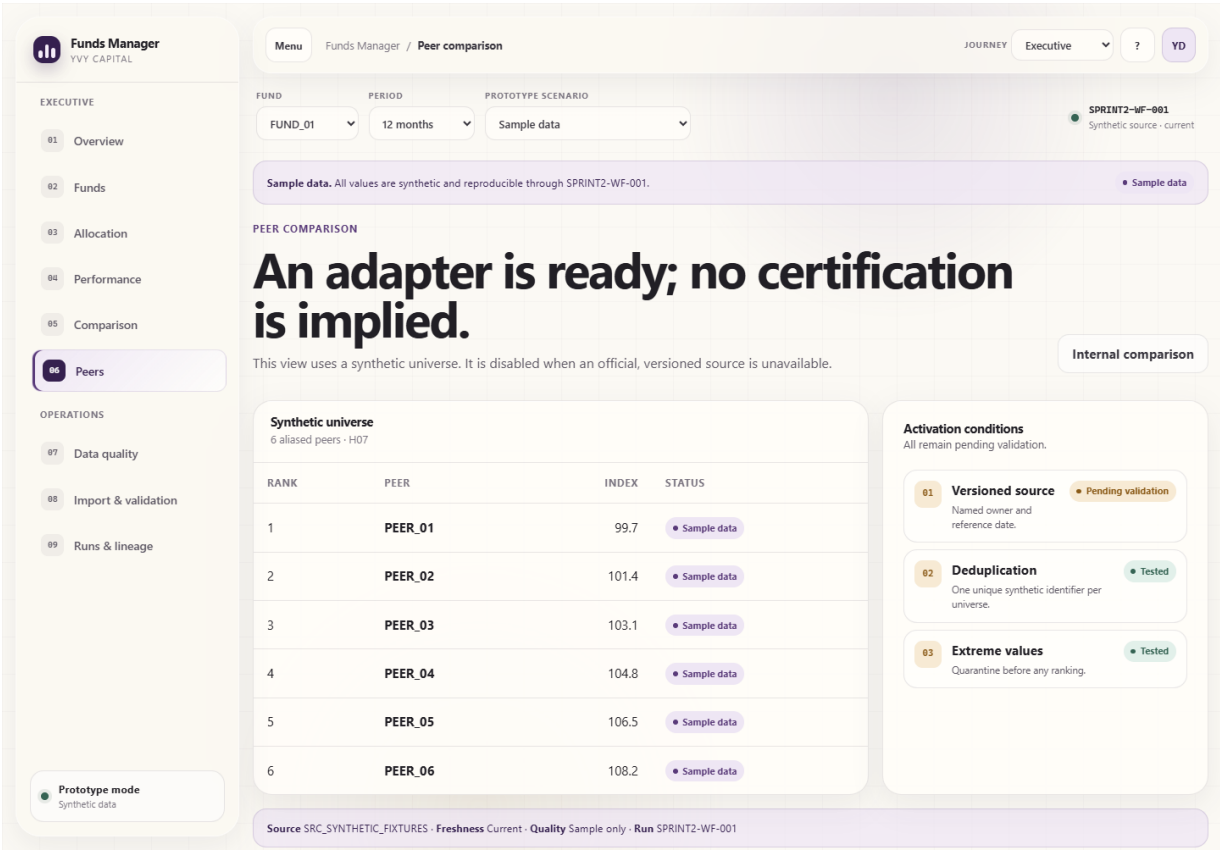


Figure 4. Synthetic peer universe with activation conditions and explicit sample-data status.

Objective / user	Provide comparative context for Executive users when a qualified peer source becomes available.
Displayed	Six aliased peers, rank, return index, and sample-data status.
Controls	Versioned source, unique universe identifier, and extreme-value quarantine conditions.
Filters / actions	Global fund, period, and scenario filters; return to Internal Comparison.
Data	Synthetic peer sample only. No real peer fund names or identifiers are exposed.
Functional interaction	Page navigation and scenario behavior are implemented; external-source activation is not.
Limits	No authorized, stable, qualified peer source or approved taxonomy is connected.
Product contribution	Provides a safe adapter concept that can be activated only after source governance is approved.
Status	Pending partner validation - source authorization, ownership, taxonomy, reference date, and outlier treatment remain open.

DASHBOARD SCREENS

Data Quality

A visible control surface for anomalies, status, severity, and opaque record references.

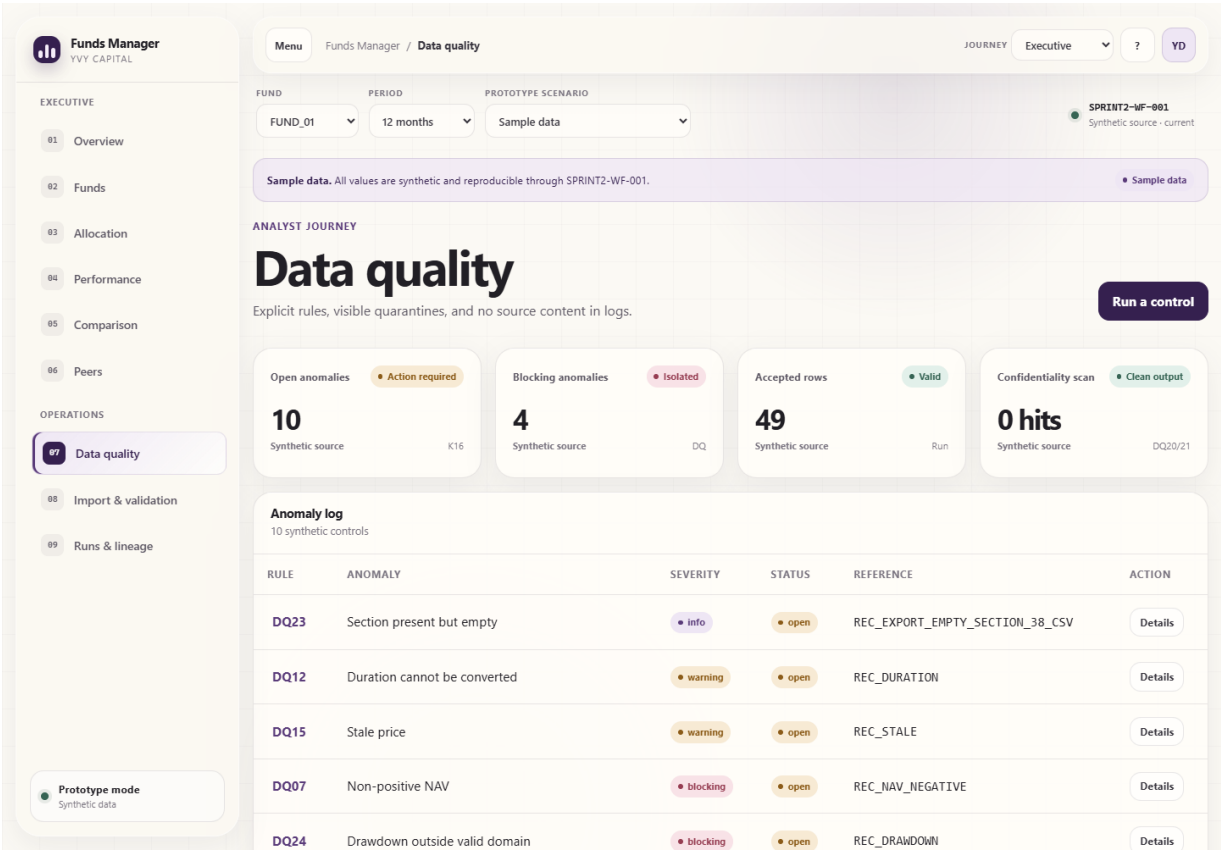


Figure 5. Data Quality view showing synthetic control counts and an anomaly log without source values.

Objective / user	Help Analysts determine whether a synthetic batch can proceed and why records are isolated.
KPIs	10 open anomalies, 4 blocking anomalies, 49 accepted rows, and 0 confidentiality hits in the current fixture run.
Table	Rule, anomaly, severity, status, opaque reference, and Details action.
Modal	Displays rule, severity, opaque reference, proposed action, and privacy disclosure; resolution and quarantine actions are simulated.
Messages	Source content is excluded from the shared log; blocking and warning states are visually distinct.
Data	Generated synthetic quality cases and deterministic run metadata.
Limits	The UI demonstrates governance behavior; it does not prove coverage of production source rules or approved tolerances.
Product contribution	Makes exceptions actionable and prepares the operational model for coded quality gates.
Status	Interactive prototype - anomaly detail and local status updates work on synthetic records.

DASHBOARD SCREENS

Import and Validation

The Analyst workflow is functional as a simulation and explicitly prevents external publication.

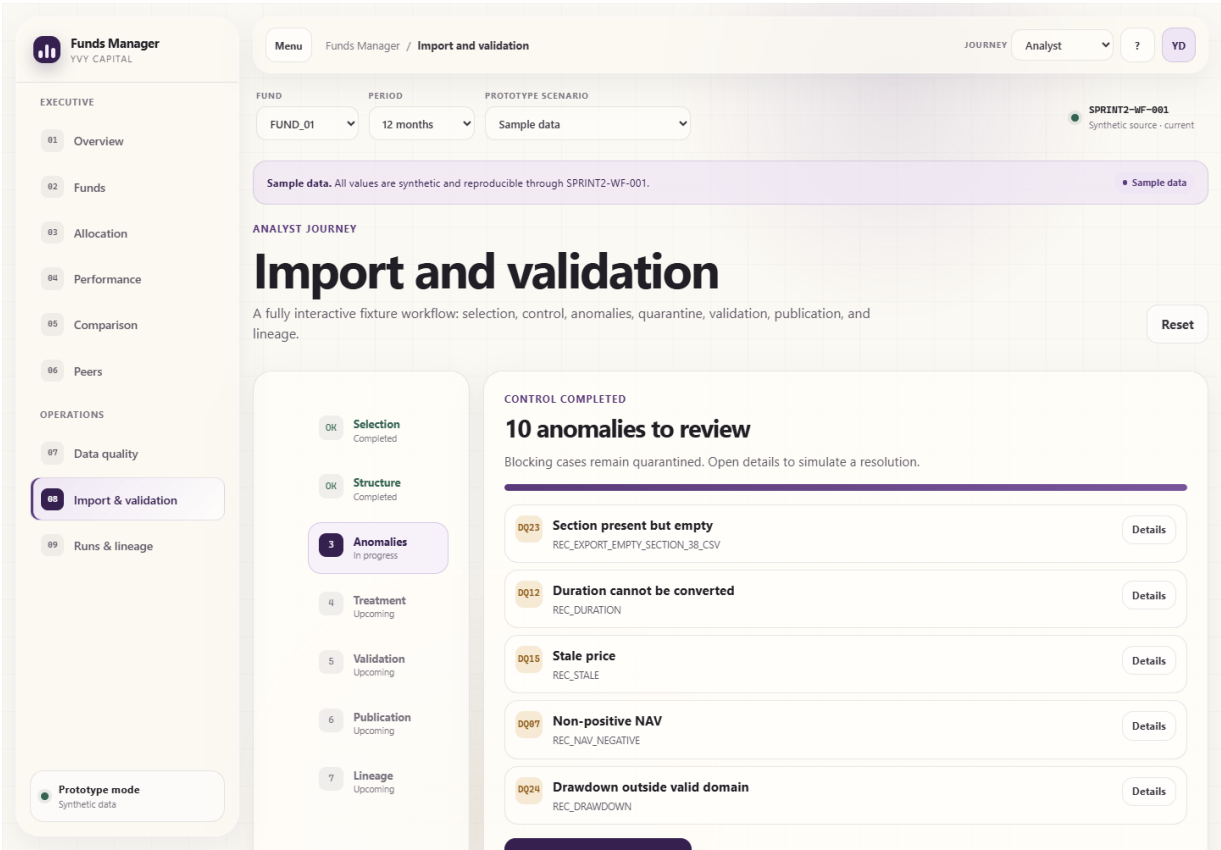


Figure 6. Analyst workflow after the structure check, with completed steps, anomalies, and actionable details.

Objective / user	Guide an Analyst from source selection to controlled local publication.
Workflow	Selection -> Structure -> Anomalies -> Treatment -> Validation -> Publication -> Lineage.
Actions	Select fixture batch, run structure check, inspect anomaly, quarantine blocking cases, validate, publish locally, and reset.
Validation	Silver/Gold contract presence, confidentiality scan, and deterministic fingerprints are presented in the simulated checklist.
Data	Three fixture shapes and a logical seven-export batch; classification remains synthetic-example.
Confirmation	Toasts confirm structure, dataset validation, and local publication; no external transfer occurs.
Limits	No file picker for production sources, human approval service, external queue, or production Serving destination.
Product contribution	Defines the safe end-to-end operating sequence required before real ingestion is enabled.
Status	Interactive prototype - all seven steps are navigable locally; production ingestion remains unimplemented.

DASHBOARD SCREENS

Run History and Lineage

A deterministic evidence path is visible without revealing source values.

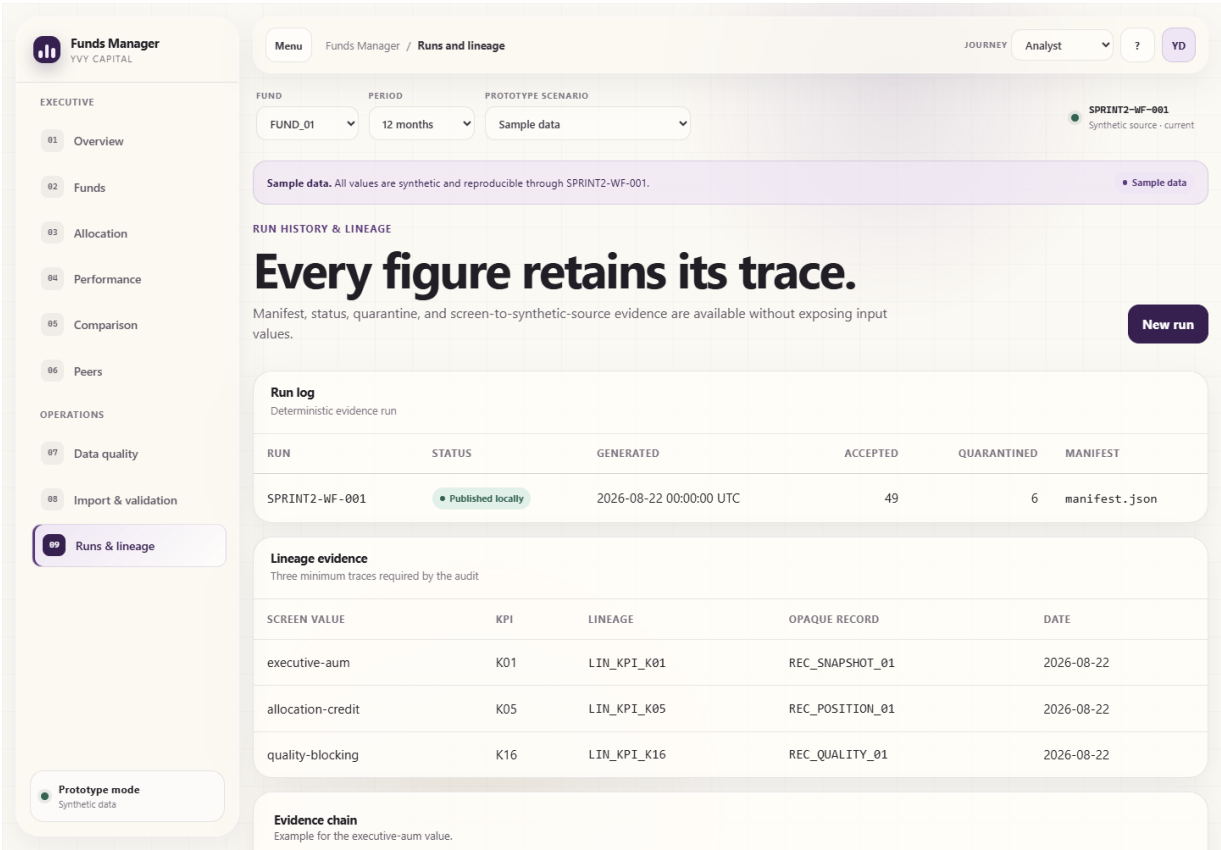


Figure 7. Run log, three screen-to-source lineage proofs, and the beginning of the evidence chain.

Objective / user	Allow Analysts and reviewers to inspect processing status and trace representative screen values.
Run table	Run identifier, local publication status, generation time, accepted count, quarantined count, and manifest reference.
Lineage table	Screen value, KPI, lineage reference, opaque record, and business date.
Evidence chain	Manifest -> Silver record -> Gold KPI -> screen value.
Actions	Start a new simulated run by returning to Import and Validation.
Data	Deterministic synthetic manifest, run, and lineage proofs.
Limits	No production orchestration history, job retries, operator identity, retention policy, or source-system audit integration.
Product contribution	Establishes the traceability pattern required for governed reporting and future audit evidence.
Status	Partially implemented - synthetic run evidence is visible; full automated lineage remains later work.

DASHBOARD SCREENS

Screen Inventory, States and Verification

All current sections are accounted for; no absent future page is counted as delivered.

Current screen	Status	Verified evidence	Current limit
Executive Overview	Implemented and visible	Portfolio signal, KPIs, chart, alerts	Synthetic portfolio only
Funds	Implemented and visible	14 aliases, search, selection, coverage	No production master data
Fund Detail / Allocation	Interactive prototype	KPI detail, donut, holdings drill-down	FUND_01 fixture baseline
Performance and Risk	Partially implemented	Chart, return, volatility, drawdown	Sharpe and duration dependencies
Internal Comparison	Implemented and visible	Seven-fund comparable table	Synthetic snapshot
Peer Comparison	Pending partner validation	Six aliased sample peers	No certified source
Data Quality	Interactive prototype	Anomaly log, modal, status actions	Synthetic control set
Import and Validation	Interactive prototype	Seven-step Analyst workflow	No production ingestion
Runs and Lineage	Partially implemented	Run and lineage evidence	No production orchestrator

State and interaction coverage

Scenarios	Sample, current, loading, late, incomplete, empty, error, access denied, no match, and hypothesis pending validation.
Interactions	Navigation, fund selection, search, allocation filter, role switch, anomaly modal, status actions, full Analyst workflow, and help notification.
Viewports	Desktop baseline and mobile layout verified; intermediate 1024 px and 768 px checks are included in final QA.
Accessibility	Skip link, semantic controls, focus transfer, arrow-key sidebar navigation, Escape behavior, labels, and screen-reader-only loading text.
Technical result	No console errors; no inline onclick handlers; no horizontal overflow at 390 px.
Implemented and visible - The test suite covers all 90 page/scenario combinations.	

USER JOURNEY

Executive User Journey

The journey prioritizes rapid orientation, progressive detail, and visible trust signals.

DECISION PATH

Overview -> prioritize a fund -> inspect allocation and holdings -> review performance -> compare internally -> open peers only when its source conditions are understood.

Journey step	What the current prototype supports	
1. Orient	Read consolidated AUM, sample performance, publication quality, alerts, source, freshness, and scenario status.	
2. Prioritize	Open the 14-fund universe and select an aliased fund based on coverage, AUM, daily return, and quality.	
3. Explain	Inspect NAV per share, concentration, price age, allocation, reconciliation concept, and filtered holdings.	
4. Evaluate	Review performance and risk indicators, including unavailable prerequisites rather than hidden substitutions.	
5. Compare	Use internal comparison first; treat the peer view as a synthetic adapter pending source validation.	
14 Aliased funds Seven also have the detailed snapshot demonstration.		6 Executive sections Overview through peer comparison.
1 Functional drill-down Allocation segment to filtered holdings.		10 Scenario states Including delayed, empty, error, denied, and hypothesis.
Implemented now	Navigation, filters, drill-down, chart/table reading, state communication, and mobile layout.	
Not final behavior	Exports, authenticated entitlements, live data, certified calculations, and decision logging.	
Partner review	Confirm priority users, five homepage KPIs, active fund universe, fund-of-funds treatment, and peer scope.	

USER JOURNEY

Analyst User Journey

The current flow demonstrates safe operating intent with synthetic fixtures and opaque references.

Step	Stage	Current behavior	Status
1	Selection	Choose the authorized synthetic fixture batch.	Interactive prototype
2	Structure	Check expected file shapes and record a deterministic outcome.	Interactive prototype
3	Anomalies	Inspect rule, severity, opaque record, and proposed action.	Interactive prototype
4	Treatment	Quarantine blocking cases without exposing source values.	Interactive prototype
5	Validation	Review contract, confidentiality, and idempotence checks.	Interactive prototype
6	Publication	Publish only to local synthetic Serving.	Interactive prototype
7	Lineage	Trace representative screen values to opaque synthetic records.	Partially implemented

Current prototype versus final operating model

Source selection	Now: a fixed synthetic batch. Final: authorized source ingestion with ownership, access, manifest, and environment controls.
Quality decision	Now: simulated local status changes. Final: coded rules, approved thresholds, durable quarantine, accountable override, and audit evidence.
Validation	Now: prototype checklist. Final: reconciled reference results, sign-off roles, and release criteria.
Publication	Now: local synthetic Serving only. Final: governed curated datasets, monitored application services, and role-based access.
Lineage	Now: three evidence proofs. Final: automated source-to-screen lineage for every published KPI.

DATA DISPLAY

KPI, Charts and Data Displayed

The prototype separates displayed values from the controls and assumptions that qualify them.

Display group	Measures	Identifiers	Visual form	Current data state
Portfolio snapshot	Gross AUM; look-through AUM; publication quality; 12-month performance	K01, K14, K16, H02	Cards + overview chart	Sample / hypothesis
Fund detail	Net assets; NAV per share; Top 5 concentration; maximum price age	K01, K02, K07, K15	Cards + allocation donut + holdings	Sample
Performance / risk	Cumulative return; volatility; maximum drawdown; Sharpe availability	H02-H05	Cards + base-100 line chart	Sample / unavailable
Comparison	AUM; relative size; daily return; volatility; quality	K01, K03, H03	Internal table	Sample
Peers	Rank; aliased peer; return index; source status	H07	Peer table	Synthetic adapter
Quality	Open anomalies; blocking; accepted rows; confidentiality hits	K16, DQ	Cards + anomaly table	Synthetic run
Runs / lineage	Accepted; quarantined; manifest; three trace proofs	Run + lineage refs	Two tables + evidence chain	Synthetic run

Display rules already applied

- Every primary screen exposes synthetic/sample status and a stable run reference.
- Freshness and quality states remain visible rather than being collapsed into a single success label.
- Unavailable prerequisites are named; the prototype does not invent a risk-free rate or duration convention.
- Peer values are separated from any certified external universe and use aliases only.
- Hard-coded sample figures support UX validation only and must not be interpreted as partner portfolio results.

INTERPRETATION RULE

Implemented and visible refers to screen behavior. It does not certify the financial values, formulas, or production data sources.

GOVERNANCE

Data Quality and Governance Elements Already Visible

Trust is communicated in the product surface while final governance remains a delivery across later sprints.

Element	Evidence currently visible	Status
Synthetic classification	Visible across the shell and source notes	Implemented and visible
Source / freshness / quality / run	Displayed in page footnotes and global status	Implemented and visible
Anomaly severity and status	Blocking, warning, info, open, quarantined, resolved	Interactive prototype
Opaque record references	Logs avoid direct source values and private identifiers	Implemented and visible
Quarantine behavior	Blocking records can be isolated in the simulation	Interactive prototype
Deterministic manifest	Stable synthetic run metadata and checksums	Partially implemented
Lineage proofs	Three screen-to-record traces and evidence chain	Partially implemented
Role journey selector	Executive / Analyst navigation shortcut only	Interactive prototype
LGPD / RBAC controls	Requirements documented but not enforced by the prototype	Planned for a later sprint

Visible evidence chain

MANIFEST SPRINT2-WF-001	SILVER REC_SNAPSHOT_01	GOLD LIN_KPI_K01	SCREEN executive-aum
----------------------------	---------------------------	---------------------	-------------------------

Confidentiality statement

This report uses dashboard screenshots containing only synthetic and aliased data. It includes no real fund names, CNPJ, private ISIN, personal data, local paths, secrets, or private repository identifiers.

FINAL PRODUCT ALIGNMENT

Alignment with the Final Product - Data and Analytics

Status is based on executed prototype evidence, not on documentation alone.

Final product capability	Current Sprint 2 W1 status	What is currently visible	What remains to be added	Target sprint	Dependency or validation
Governed ETL pipeline	Partially implemented	Deterministic local synthetic run and manifest	Production-grade ingestion, orchestration, error recovery, operating controls	Sprint 3 v1; Sprint 5 final	Approved sources and environment
Raw/Bronze, Silver, Gold, Serving	Partially implemented	Contracts and Silver -> Gold -> Serving evidence	Persistent governed layers, ownership, retention, deployment	Sprint 3	Interface contracts and storage choice
Portfolio-source ingestion	Interactive prototype	Fixture selection and structure check	Authorized connectors, secure landing, schema evolution, replay	Sprint 3	Source inventory and access
NAV and portfolio monitoring	Partially implemented	Overview, fund cards, allocation, holdings	Live curated NAV/positions, reconciliation, alerts	Sprint 3 alpha	Fund universe and source mapping
Performance indicators	Partially implemented	Sample return and base-100 chart	Certified modules, reference cases, production history	Sprint 3 alpha	Formula approval and benchmarks
Risk-return analysis	Partially implemented	Volatility/drawdown samples; Sharpe unavailable	Sharpe/Sortino, liquidity, stress, DV01 as prioritized	Sprint 4	Risk-free rate, units, thresholds
Internal fund comparison	Interactive prototype	Seven-fund comparison table	Certified common-date measures and exclusion rules	Sprint 3 alpha	Active universe and validation cases
Peer comparison	Pending partner validation	Synthetic six-peer adapter view	Qualified source, taxonomy, outlier rules, approved universe	Sprint 4 conditional	Source authorization and availability
Automated reconciliation	Specified but not yet visible	Reconciliation concept only	Positions + cash + provisions vs NAV with exceptions	Sprint 4	Tolerance and accounting rules
Data-quality controls	Partially implemented	Synthetic rules, anomaly log, reports	Production rule coverage, ownership, thresholds, alerts	Sprint 3-Sprint 4	Approved domains and tolerances
Anomaly quarantine	Interactive prototype	Simulated quarantine and opaque log	Durable quarantine, override workflow, accountable release	Sprint 3	Decision rights and retention

Status language follows the seven-level scale defined for this report. Target sprints come from the approved planning sequence; uncertain production decisions are not assigned invented dates.

FINAL PRODUCT ALIGNMENT

Alignment with the Final Product - Governance, Operations and Handover

The role selector and local run evidence are not substitutes for enterprise security or production operations.

Final product capability	Current Sprint 2 W1 status	What is currently visible	What remains to be added	Target sprint	Dependency or validation
Lineage and run history	Partially implemented	One synthetic run and three trace proofs	Automated lineage for every output, retries, operator audit	Sprint 3-Sprint 4	Orchestrator and metadata model
Source freshness	Interactive prototype	Current, late, incomplete states and price age	Source-specific SLAs, monitoring, escalation	Sprint 3-Sprint 4	Partner-approved thresholds
Authentication	Specified but not yet visible	No authentication; demonstration profile only	Approved identity provider and secure sessions	Sprint 4	Hosting and identity decision
Role-based access control	Specified but not yet visible	Journey selector changes navigation only	Enforced roles for import, validate, export, and detail	Sprint 4	Role matrix approval
LGPD and anonymization	Partially implemented	Aliases, opaque references, synthetic-only output	Policy enforcement, access tests, retention, approved export rules	Sprint 4	Data classification and security review
Production data connections	Out of scope for Sprint 2 Week 1	None	Authorized connectors and environment-specific configuration	To be confirmed	Source owners, credentials, hosting
Exports and reporting	Specified but not yet visible	No PDF/CSV export action	Filtered, dated, logged, role-controlled outputs	Sprint 5 / To be confirmed	Export policy and templates
Monitoring and observability	Specified but not yet visible	Local run status only	Health, DQ trends, job alerts, performance telemetry	Sprint 5	Deployment architecture
User documentation	Planned for a later sprint	Prototype labels and this progress report	Usage guide, known limits, release-aligned screenshots	Sprint 5; draft Sprint 4	Stable beta workflows
Maintenance documentation	Planned for a later sprint	Architecture and operating concepts	Deployment, replay, monitoring, ownership, troubleshooting	Sprint 5	Final architecture and operations
Testing, deployment and handover	Partially implemented	Automated synthetic tests and responsive QA	UAT, security, performance, installation, release, knowledge transfer	Sprint 3-Sprint 5	Environments, users, acceptance baseline

Authentication, RBAC, production connections, monitoring, exports, manuals, deployment, and final handover are not represented as completed by the prototype.

FORWARD PLAN

Next Additions Not Yet Visible in the Dashboard

Each horizon distinguishes the current mock-up from the final behavior expected by the roadmap.

Horizon	Description	Business reason	Prerequisite	Priority	Current status	Prototype-to-final difference
Remainder of Sprint 2	Validate users, screen baseline, homepage KPIs, source matrix, 7/14-fund treatment, fund-of-funds bridge, peer scope, and Sprint 3 backlog.	Prevents rework before alpha development.	Partner review and decision log	Must	Pending partner validation	Today: proposed UI and assumptions. Final S2 outcome: approved or explicitly changed baseline.
Sprint 3	Build pipeline v1, governed layers, production-shaped ingestion, coded DQ gates, alpha services, reference tests, and automated lineage.	Creates a reproducible vertical slice from approved input to screen.	Approved contracts, sources, KPI cases	Must	Planned for a later sprint	Today: fixtures and local evidence. Final S3 behavior: automated import -> control -> KPI -> alpha screen.
Sprint 4	Add advanced risk, reconciliation, controlled peers, RBAC, LGPD controls, audit evidence, end-to-end tests, and UAT.	Makes the beta analytically useful and safe for pilot validation.	Stable alpha, identity, qualified peer source or adapter decision	Must / conditional peers	Planned for a later sprint	Today: visual placeholders and samples. Final S4 behavior: governed integrated beta with acceptance evidence.
Sprint 5	Stabilize release, monitoring, regression evidence, exports as approved, user/maintenance manuals, deployment, and handover.	Enables repeatable operation without implicit team knowledge.	Accepted beta and frozen scope	Must	Planned for a later sprint	Today: working prototype. Final S5 behavior: release package, controlled deployment, manuals, and accepted transfer.

Remaining Work by Sprint

Sprint 2	Partner decisions, source-of-truth reconciliation, approved prototype baseline, and sprint-ready backlog.
Sprint 3	Reproducible data pipeline and working MVP alpha for NAV, portfolio, performance, and internal comparison.
Sprint 4	Integrated analytics beta, risk, reconciliation, conditional peers, security, LGPD, and UAT.
Sprint 5	Stabilization, release, monitoring, complete documentation, final demonstration, and handover.
Pending partner validation - The Sprint 2 exit gate remains open until decisions are recorded.	

CONTROL POINTS

Dependencies and Pending Partner Decisions

Open decisions should be resolved before irreversible Sprint 3 implementation choices are made.

ID	Decision	Required outcome	Decision owner
D1	Priority users and journeys	Confirm Executive and Analyst baseline; identify any required Manager or Auditor path.	YvY Capital
D2	Homepage KPI set	Approve the five most important metrics and their interpretation conventions.	YvY Capital + Analytics
D3	Fund universe	Resolve seven snapshot funds versus fourteen funds with historical coverage.	YvY Capital + Data
D4	Fund-of-funds bridge	Approve relationships, look-through treatment, and double-counting controls.	YvY Capital
D5	Calculation and DQ thresholds	Approve benchmark, risk-free rate, duration units, freshness, and NAV reconciliation tolerance.	YvY Capital + Analytics
D6	Peer source	Confirm authorization, stability, taxonomy, outlier handling, and delivery timing.	YvY Capital
D7	Access model	Define who can import, validate, export, and view detailed positions.	YvY Capital + Security
D8	Environment	Confirm hosting, identity provider, source access, and demonstration constraints.	YvY Capital + Inteli

Risks and Current Limitations

Risk / limitation	Potential impact	Current control / response	Level
Late or fragmented review	Rework or delayed alpha	Consolidated W4 decision set and bounded corrections	High
7/14-fund ambiguity	Model and test scope diverge	Support 14 with a configurable approved subset	High
Unqualified calculations or peers	Misleading comparison	Block unsupported metrics; retain explicit sample/pending states	High
Sensitive data exposure	Confidentiality / LGPD impact	Authorized private environment, aliases, RBAC, output scanning	Critical
Prototype mistaken for production	Incorrect business reliance	Working Draft and synthetic disclosures on report and UI	High
Integration deferred too long	Unstable beta	Freeze contracts in Sprint 2 and integrate continuously from Sprint 3	Medium

CLOSEOUT

Recommended Next Steps

A short sequence keeps partner decisions early and protects the Sprint 3 critical path.

- 1. Review the translated prototype with YvY Capital using the Executive and Analyst scenarios shown in this report.
- 2. Record D1-D8 as Accepted, Accepted with bounded changes, Not approved, or Deferred, with owner and date.
- 3. Freeze the priority screen baseline, fund universe, KPI definitions, source matrix, and peer treatment at the Sprint 2 gate.
- 4. Convert approved stories into Sprint 3 work with owner, estimate, fixture, acceptance command, reviewer, and dependency owner.
- 5. Begin the Sprint 3 vertical slice with authorized data: ingestion -> controlled layers -> DQ -> KPI -> alpha screen -> lineage evidence.
- 6. Keep the prototype and all project evidence in the authorized private environment and preserve synthetic data for demonstrations.

Conclusion

Sprint 2 Week 1 has produced a complete English prototype baseline with nine live sections, two coherent user journeys, explicit degraded states, functional drill-down, and visible governance cues. This is meaningful progress toward the Funds Manager product direction.

The evidence also makes the boundary clear: the current dashboard uses synthetic fixtures and simulated operating logic. Production ingestion, certified financial calculations, automated reconciliation, enterprise access control, monitoring, UAT, deployment, and handover remain later-sprint work.

RECOMMENDED GATE OUTCOME

Use this report and the translated dashboard as a Working Draft for partner review. Move to Sprint 3 development only after the priority screen set, KPI conventions, source scope, security assumptions, and conditional peer strategy are explicitly recorded.

Pending partner validation - No approval or partner acceptance has been fabricated or implied.

Prepared on August 22, 2026 | Inteli × YvY Capital | Funds Manager
